

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Project: EV Charging Station Reservation System

Siddhant Khurdiya | PES1UG24AM275 | PES University — Dept. of CSE

Sprint 1 Summary

Sprint 1 included 6 user stories drawn from Epic 1 (Charging Slot Discovery & Reservation), Epic 2 (Dynamic Pricing & Payment), and Epic 4 (Station Operator Management), totaling 29 story points. All 6 stories were moved to Done by the end of the sprint.

Story	Epic	Priority	Points	Sprint 1 Outcome
1.1 Connector Matching	Epic 1	High	3	Done
1.2 Real-Time Availability	Epic 1	High	5	Done
1.3 Slot Reservation	Epic 1	High	8	Done
2.1 Dynamic Rate Display	Epic 2	Medium	5	Done
4.1 Charger Maintenance Toggle	Epic 4	High	3	Done
4.2 Instant Availability Update	Epic 4	High	5	Done

Reflection Questions

1. Did your estimations reflect the actual effort?

Mostly yes. Simpler, well-defined stories like Connector Matching (3 points) and the two operator-side toggles (3 and 5 points) matched their estimated complexity closely, since they involved fairly direct status/matching logic. The higher-point stories — Slot Reservation (8 points) and Dynamic Rate Display (5 points) — were harder to estimate precisely upfront because they involve more interdependent logic (concurrency handling for reservations, and multi-factor pricing calculations). In hindsight, Slot Reservation's estimate feels roughly right given it touches booking, locking, and confirmation all at once, but it would benefit from being split into smaller sub-stories in a real (non-simulated) sprint.

2. Was your backlog well-prioritized?

Yes. The High-priority stories were the ones that unlock everything downstream: without connector matching, real-time availability, and slot reservation working, there is no booking flow to attach pricing or notifications to. Similarly, the operator-side stories (marking chargers under maintenance, instant availability updates) were also marked High since inaccurate availability data would break the driver-facing experience. Medium-priority stories like payment processing and notifications were correctly sequenced into Sprint 2, since they depend on a working reservation flow existing first. Low-priority items like the no-show penalty alert were left for later since they only matter once the core booking loop is already functioning.

3. How did your simulated sprint align with your plan?

The sprint aligned with the plan in terms of scope — all 6 planned stories were completed and moved to Done. However, because this was a simulated sprint completed in a single working session rather than across an actual week, the pace of completion doesn't reflect how a real team would burn down work day by day. In a real sprint, I'd expect the reservation and pricing stories to take noticeably longer than the operator toggle stories, given their added complexity around concurrency and calculation logic.

4. What insights did the burndown chart give about your team's capacity?


The burndown chart showed the remaining work dropping sharply and early (all 29 points cleared within the first day or two of the sprint window) rather than declining gradually along the grey guideline line. Read literally, this pattern usually signals that the team either finished work faster than planned or that the sprint's timeline didn't match

how the work was actually executed — in this case, the latter, since the simulation was compressed into one sitting instead of spread across the full week. It's a useful reminder that a burndown chart is most informative when work is logged as it genuinely happens; simulating everything at once (or in two sittings) produces a chart shape that looks like an early finish even when the estimates themselves were reasonable. For a real sprint, I would expect a smoother, more staggered decline as different team members complete stories on different days.

Deliverables Checklist

- Screenshot: Jira Backlog with Epics and User Stories
- Screenshot: Story Point Assignments
- Screenshot: Sprint Board (Active Sprint view)
- Screenshot: Burndown Chart
- This reflection document

Deliverable 1: Jira Backlog with Epics & User Stories

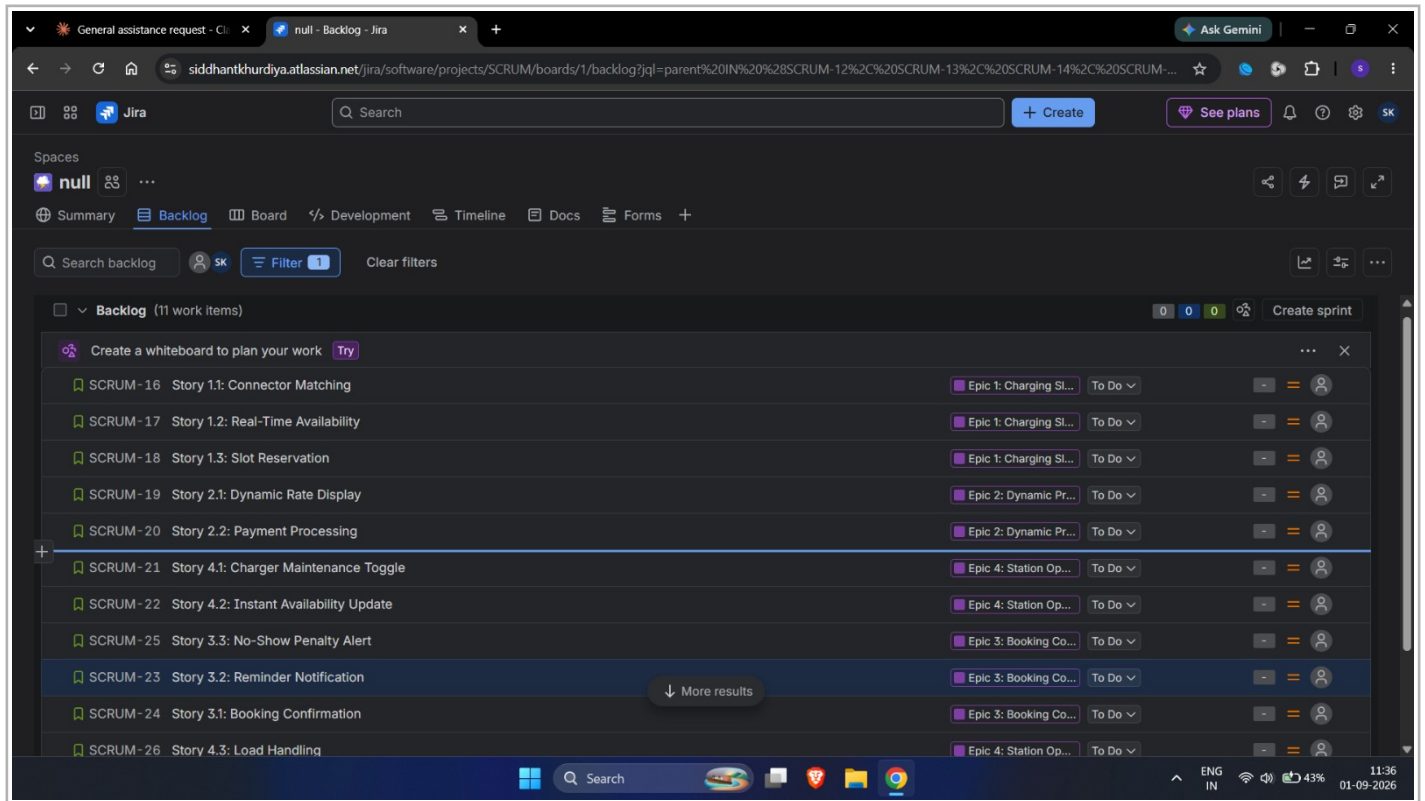

All 4 Epics and 11 User Stories, correctly linked (Epic tags visible on each story).


Deliverable 2: Story Point Assignments

The screenshot displays a Jira backlog for a project named 'null'. The backlog contains 11 work items, each representing a user story. Each story is assigned a story point value (Fibonacci scale) and a priority indicator (To Do, In Progress, Done). The stories are listed in a table format with columns for the story key, story title, epic, status, points, and priority.

Story Key	Story Title	Epic	Status	Points	Priority
SCRUM - 16	Story 1.1: Connector Matching	Epic 1: Charging Si...	To Do	3	High
SCRUM - 17	Story 1.2: Real-Time Availability	Epic 1: Charging Si...	To Do	5	High
SCRUM - 18	Story 1.3: Slot Reservation	Epic 1: Charging Si...	To Do	8	High
SCRUM - 19	Story 2.1: Dynamic Rate Display	Epic 2: Dynamic Pr...	To Do	5	Medium
SCRUM - 20	Story 2.2: Payment Processing	Epic 2: Dynamic Pr...	To Do	8	Medium
SCRUM - 21	Story 4.1: Charger Maintenance Toggle	Epic 4: Station Op...	To Do	3	High
SCRUM - 22	Story 4.2: Instant Availability Update	Epic 4: Station Op...	To Do	5	High
SCRUM - 25	Story 3.3: No-Show Penalty Alert	Epic 3: Booking Co...	To Do	2	Low
SCRUM - 23	Story 3.2: Reminder Notification	Epic 3: Booking Co...	To Do	3	Medium
SCRUM - 24	Story 3.1: Booking Confirmation	Epic 3: Booking Co...	To Do	2	Medium
SCRUM - 26	Story 4.3: Load Handling	Epic 4: Station Op...	To Do	13	Medium


Story points (Fibonacci scale) and priority indicators assigned to every story.

Deliverable 3: Sprint Board (Active Sprint View)

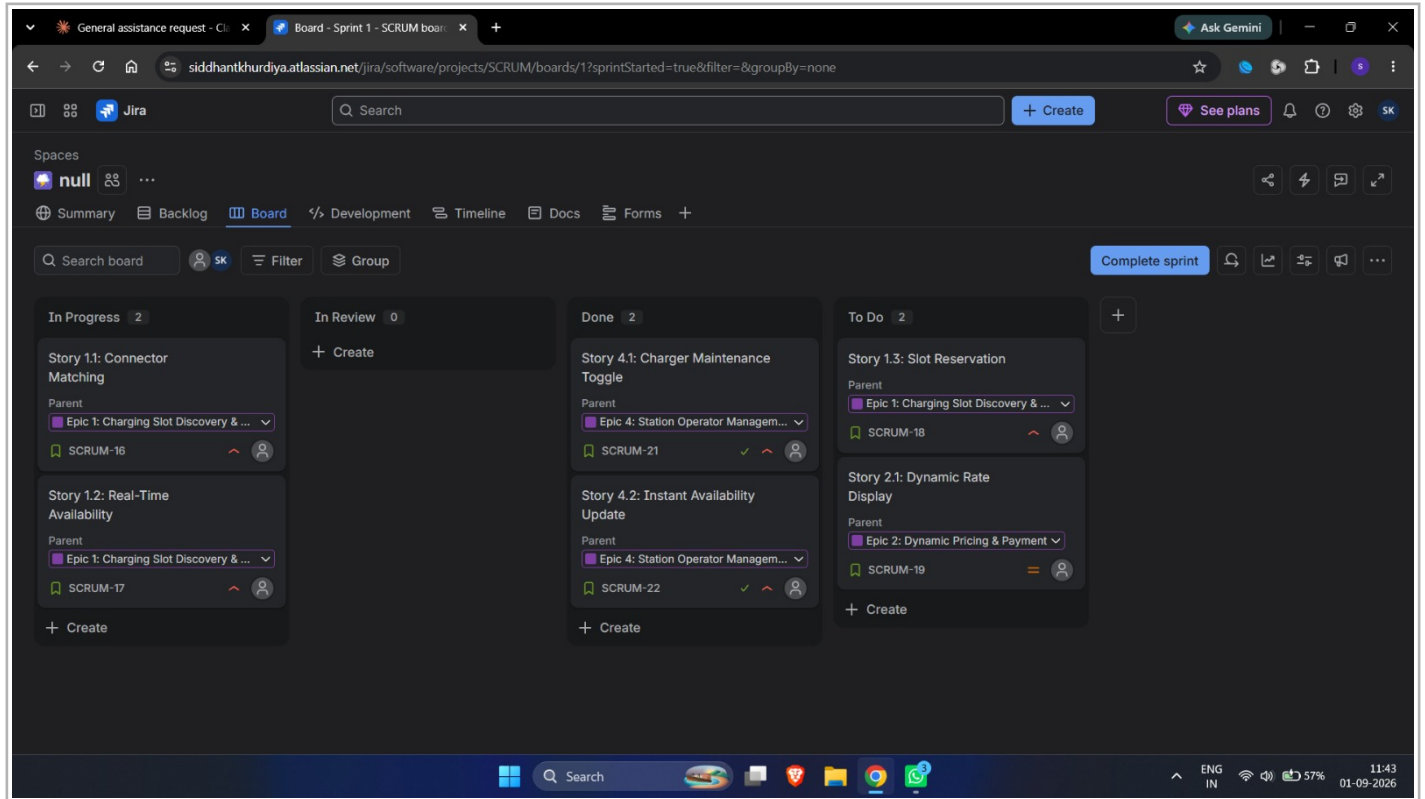


Sprint 1 mid-progress: stories distributed across In Progress, Done, and To Do.

Deliverable 4: Burndown Chart

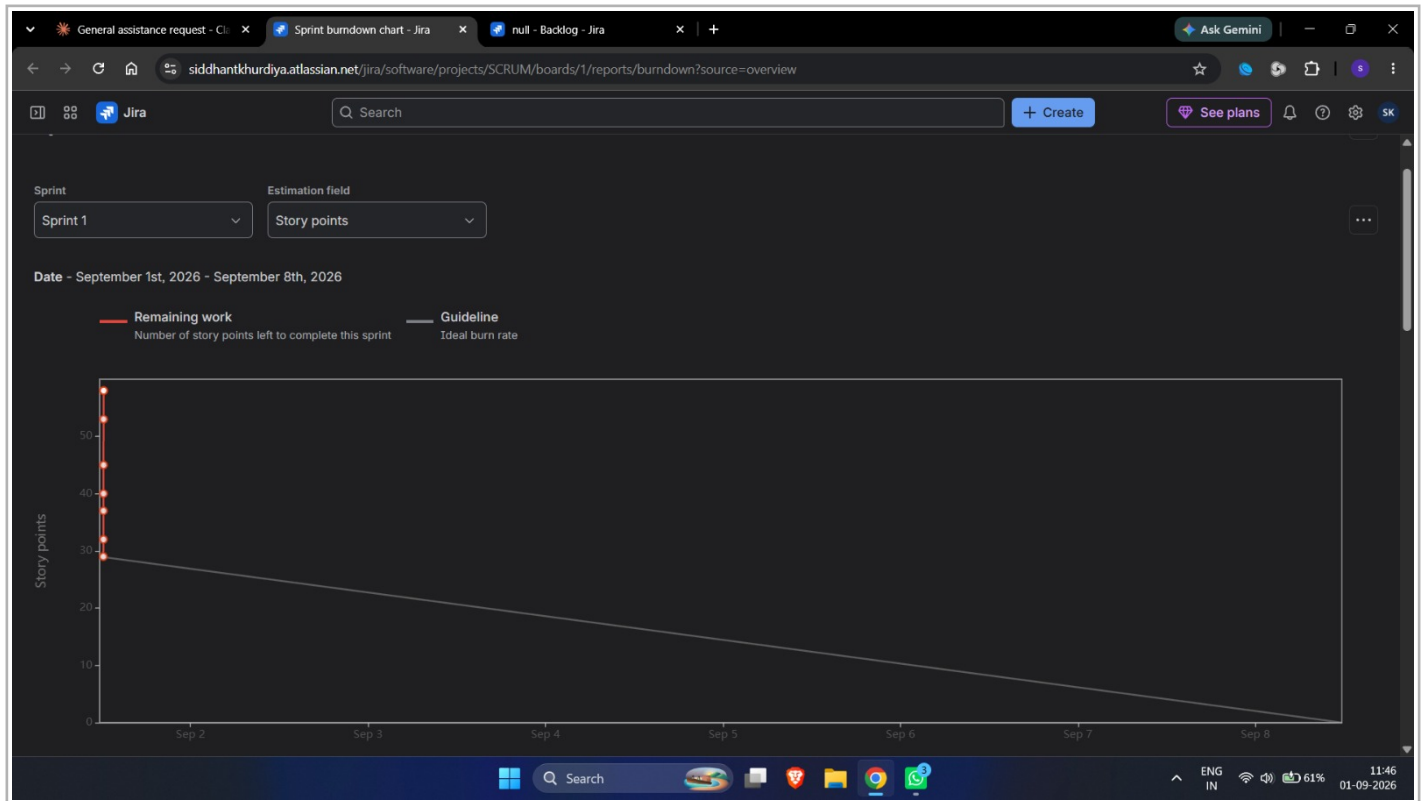

Sprint 1 burndown showing remaining story points against the ideal guideline.

Deliverable 5: Project Summary

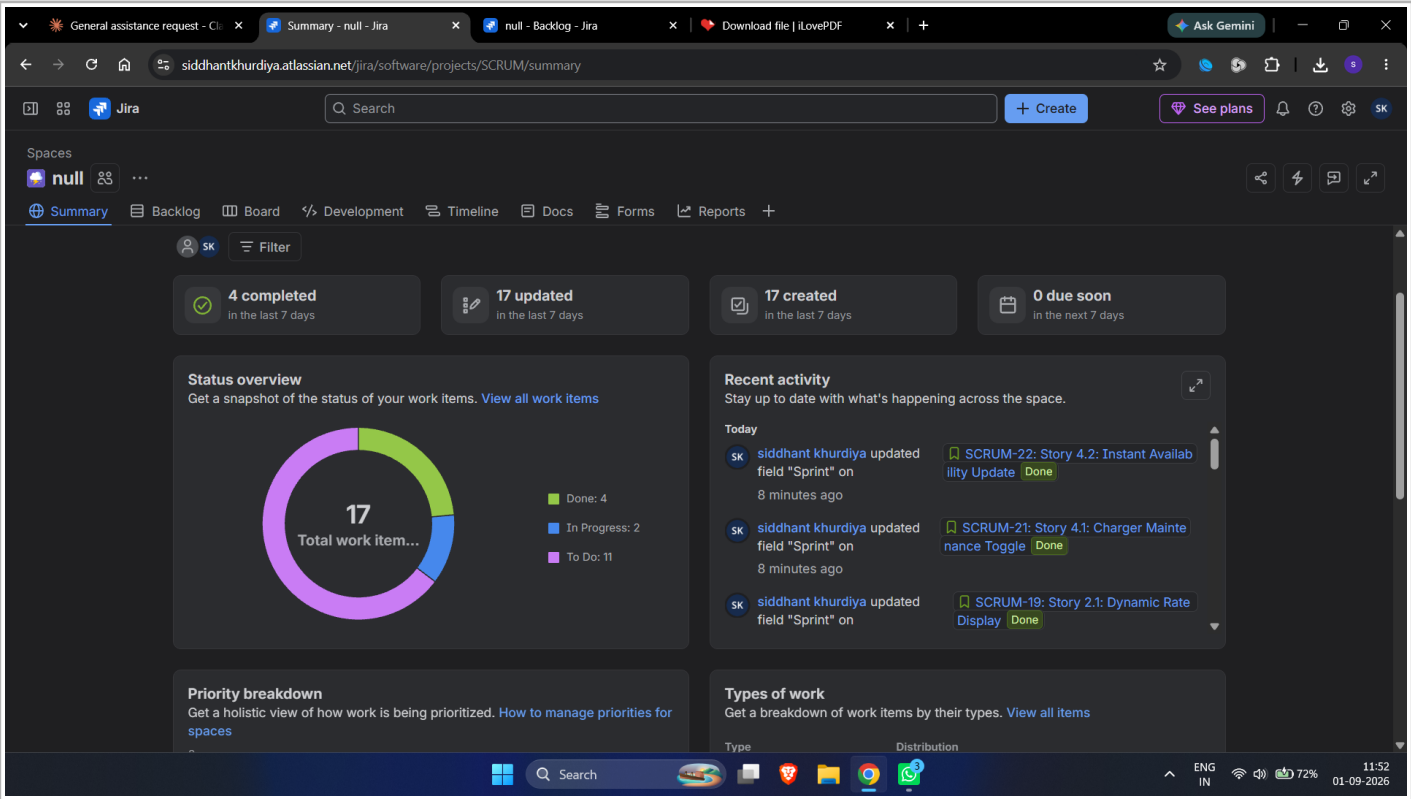

Overall status overview: 17 total work items, 4 done, 2 in progress, 11 to do.
